

Project Name: Lohia One
UP RERA Registration No. UPRERAPRJ977450/06/2025
Website of UP RERA: www.up-rera.in
Launch Date: 03-06-2025



Collection A/C Details Of Lohia One:
Bank Account Name: Lohia Developers (India) Pvt. Ltd. collection account for
Account Number: 43711463236
Bank Name: State Bank Of India
IFSC Code: SBIN0004113



*All images shown in this leaflet are for illustration purpose only

AUGUST 2026

**EXCLUSIVE VILLA
COMMUNITY.**

**CONSTRUCTION UPDATES
OF YOUR FUTURE VILLA.**

NEW MORADABAD

To know more visit www.lohiaworldspace.com or call +91 70 80 90 60 60

LOHIA WORLDSPACE

Lohia Worldspace is committed to creating expansive spaces that offer more than just room to live—they create room to connect, breathe, and belong.

We believe in designing environments where modern amenities coexist seamlessly with the gifts of nature, fostering a deep sense of belonging and pride. Every space is thoughtfully envisioned to offer an experience rooted in comfort, luxury, and leisure, while maintaining harmony with the natural world.

Our endeavor is to move beyond the conventional concrete landscape and create communities where architecture and nature exist in balance. Thoughtful planning, generous open spaces, and flourishing greenery come together to break the monotony of built environments, uplift the spirit, and inspire meaningful connections.

At Lohia Worldspace, we don't simply create spaces. We create expansive experiences where luxury meets nature and where every place feels like it truly belongs to you.



Exclusive Villa Community.

Where, Every Home Has

Modern Interiors

Spacious Rooms

Independent Stairs

Open Space

Club House with Amenities

घर हो,
VILLA
JAISA.



CONSTRUCTION UPDATES



Temple (Mandir)

All civil and structural works, including internal and external plastering works, have been completed. The front landscape works are also nearing completion.



Main Gate and Guard Room

Civil works for the main gate foundations and plinth beam at the exit side have been completed, while the corresponding works at the entry side are in progress. The MS structure for the canopy over the guard room roof has also been installed.

CONSTRUCTION UPDATES



Villa A01 to A12

Villa Works Plinth beam casting for all villas has been completed. Ground floor roof slab works for Villas A07 to A12 have been completed, while Mivan shuttering and reinforcement works for the ground floor roof slabs of Villas A05 and A06 are currently in progress.

CONSTRUCTION UPDATES



Villa A13 to A24

Ground floor roof slab works for all 12 villas have been completed. First floor roof slab works for Villas A17 to A24 have also been completed, while Mivan shuttering and reinforcement works for the first floor roof slabs of Villas A15 and A16 are currently in progress.

CONSTRUCTION UPDATES



Villa A25 to A34

All structural works from ground floor to mumty level for all 10 villas have been completed. The front brick-tile façade works for Villas A31 to A34 have also been completed, while brickwork for the remaining villas is currently in progress.

CONSTRUCTION UPDATES



Sample Villa A35 and A36

All works, including finishing and interior works, for Sample Villa A36 have been completed. For Lead Villa A35, all finishing works have been completed, while interior works are currently in progress and are expected to be completed by the end of September.



Villa A37 to A44

Ground floor roof slab works for all 6 villas have been completed. First floor roof slab works for 5 out of 6 villas have also been completed, while mummy roof slab works for 4 out of 6 villas have been completed to date.

CONSTRUCTION UPDATES



Villa B01 to B32

Plinth beam casting works for all 32 villas have been completed. Ground floor roof slab works for Villas B11 to B16 have also been completed, while first floor roof slab works for Villas B15 and B16 are currently in progress.

CONSTRUCTION UPDATES



Villa B33 to B58

Plinth beam casting works for all 26 villas have been completed. Ground floor and first floor roof slab works for Villas B46 and B47 have also been completed, while mummy slab shuttering works are currently in progress.



Villa C01 to C26

Foundation casting and pedestal works are currently in progress.

CONSTRUCTION UPDATES



Villa C27 to C58

All foundation works, along with soil filling, have been completed. Plinth beam casting works for 14 villas have been completed to date. Ground floor roof slab works for Villas C39 to C43 have also been completed, while the first floor roof slab of Villa C43 has been completed. Mivan shuttering and reinforcement works for the ground floor roof slabs of Villas C37 and C38 are currently in progress, along with first floor roof slab works for Villas C41 and C42.



Club One

Raft concrete works were completed in the previous month. Reinforcement, shuttering, and concreting works for the shear walls, basement slabs, STP tanks, and other water tanks are currently in progress.

CONSTRUCTION UPDATES



Boundary Wall

Approximately 85% of Entire Boundary Wall construction has been completed along with Plastering works in 75% of walls.



Concrete Compressive Strength Test

The Concrete Compressive Strength Test is conducted to determine the ability of hardened concrete to withstand compressive loads, which is a key indicator of its strength and quality. Concrete cubes are cast and cured for specified periods, commonly 7 and 28 days, and then tested in a compression testing machine until failure. The compressive strength is calculated and expressed in MPa. The test is carried out as per IS 516 to assess whether the concrete meets the specified design strength and structural requirements.

CONSTRUCTION UPDATES



TMT Tensile Strength and Elongation Test

The Reinforcement (TMT) Tensile Strength and Elongation Test is conducted to determine the yield strength, ultimate tensile strength, and ductility (percentage elongation) of steel reinforcement bars. The test assesses the ability of the reinforcement to withstand tensile forces and undergo deformation without sudden failure. In this test, a steel specimen is subjected to a gradually increasing tensile load in a Universal Testing Machine (UTM) until it fractures. The tensile strength and percentage elongation are then determined from the test results. The test is carried out as per IS 1608 to confirm the quality, strength, and suitability of the reinforcement for structural applications.



Concrete Slump Test

The Concrete Slump Test is a simple field test used to measure the workability and consistency of fresh concrete by filling a standard slump cone in layers, compacting each layer, and then lifting the cone to observe the amount the concrete subsides (slump); the result indicates how easily the concrete can be mixed, placed, and compacted, and is commonly performed as per IS 1199 and IS 7320.

CONSTRUCTION UPDATES



Cement Finess Test

The Cement Finess Test is conducted to determine the fineness or particle size distribution of cement, which influences its rate of hydration, strength development, and workability. The test is commonly performed using the 90-micron sieve method or the air permeability method using a Blaine apparatus. The test is carried out as per IS 4031 (Part 1). Finer cement generally provides faster hydration and early strength development, although it may increase water demand and affect the workability of the concrete.



Slab Inspection during and after Casting

Slab inspection is carried out during and after casting to verify the reinforcement, shuttering, concrete placement, level, thickness, compaction, and curing. The inspection ensures that the slab is constructed in accordance with the specified drawings, quality standards, and structural requirements.

CONSTRUCTION UPDATES



Curing of Walls and Slabs

Walls and slabs are continuously cured for a minimum period of 7 days in accordance with IS 456:2000 (Clause 13.5). Adequate moisture is maintained through suitable curing methods such as ponding, wet hessian, or other approved methods. Proper curing ensures the development of the required concrete strength and helps prevent shrinkage cracks and other defects.



RMC Plant Inspection and Calibration:

Regular inspection and calibration of the RMC plant are carried out to ensure accurate batching, weighing, mixing, and proportioning of cement, aggregates, water, and admixtures. All weighing systems, moisture sensors, water meters, and admixture dosing systems are periodically calibrated, with valid calibration certificates maintained for verification. The plant is also inspected for proper functioning, cleanliness, material storage, and effective material control. These measures help ensure consistent concrete quality in accordance with IS 4926:2003 and IS 456:2000.

CONSTRUCTION UPDATES



Alcohol Test

The significance of alcohol testing at a construction site is to ensure workers are fit for duty, prevent accidents caused by impaired judgment, comply with HSE and contractual requirements, and protect the safety of workers, equipment, and the public



Training for House Keeping and Safety Techniques

Regular training is provided to site personnel on proper housekeeping, material stacking, waste removal, maintaining clear access routes, PPE usage, hazard identification, and safe working practices to maintain a clean, organized, and safe workplace and prevent accidents.

CONSTRUCTION UPDATES



Tool Box techniques (TBT)

Toolbox Talks (TBT) are regularly conducted at the workplace by the Contractor's Safety Officer to brief site personnel on the safety precautions to be followed while working at the site. TBTs are conducted before the start of work and involve both technical staff and labour.



Mosquito Fogging at Labour Camp

Regular mosquito fogging has been carried out at the labour camp and surrounding areas to control mosquito breeding, minimize the risk of vector-borne diseases, and maintain a hygienic and healthy living environment for workers.



Township Entrance & Exit



Theme Garden



Club One



Kids Area




Open Yoga



Cricket Pitch



Basketball Court

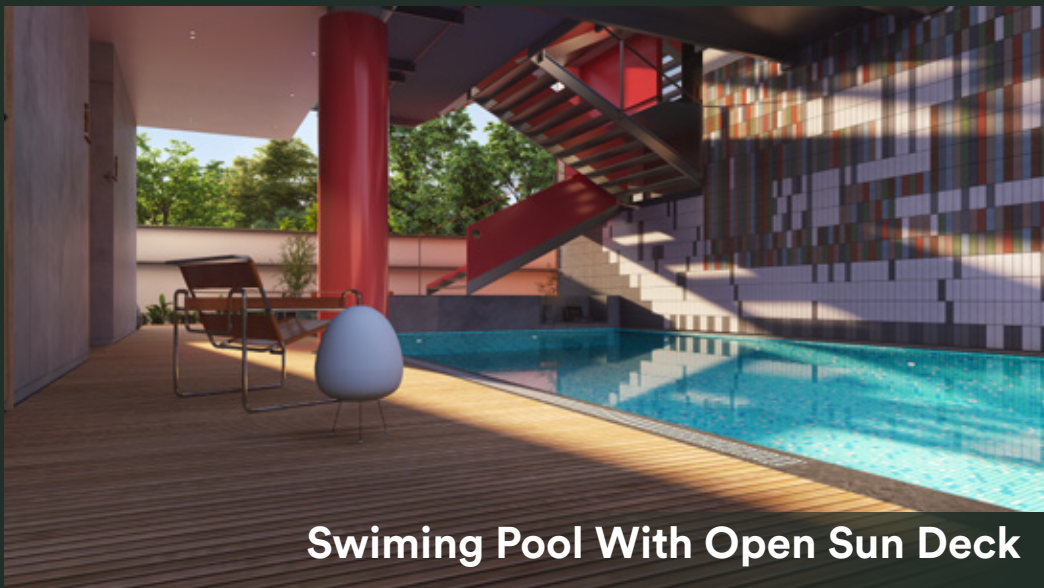

Swimming Pool With Open Sun Deck




Indoor Gym



Indoor Squash Court



Indoor Badminton Court

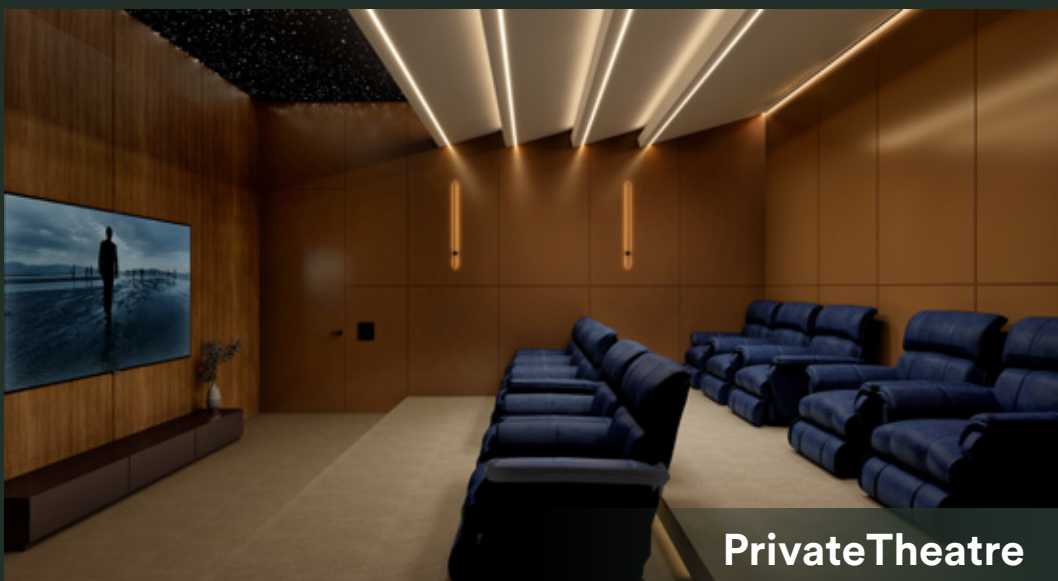

Private Theatre

Refer & Rejoice

Your Trust Deserves a Reward!

At Lohia One, we believe our happiest customers are our best ambassadors. Now, when you refer someone to us it's not just a gesture, it's a celebration!

HOW IT WORKS:

Share a Genuine Lead: Tell your friends, family, or colleagues about Lohia One.

They Book a Home: Once your referred lead successfully books with us

You Earn

₹ 50,000*

They Save

₹ 100,000*

SIMPLE STEPS:

1. Share your friend's contact details with our CRM team before their first visit.
2. Our team will personally connect with them and assist in their home-buying journey.
3. Once the booking is confirmed and minimum 30% payment is completed, your reward will be processed.

Important Conditions: (a) The referred lead should be exclusive and not associated with any other channel partner, dealer, or reference. (b) The referee's benefit and referrer's reward will be applicable only after 30% of the booking amount is received.

The management reserves the right to verify and validate all referrals.



EXCLUSIVE VILLA COMMUNITY

घर हो,
**VILLA
JAISA.**

New Moradabad

+91 70 80 90 60 60

hello@lohiaworldspace.com

* T/C are applied.

Project Name: Lohia One, Launch Date: 03-06-2025
UP RERA Registration No. UPRERAPRJ977450/06/2025, Website of UP RERA: www.up-rera.in,
Collection A/C Details Of Lohia One:
Bank A/C Name: Lohia Developers (India) Pvt. Ltd. collection account for Lohia One
Account Number: 43711463236, Bank Name: State Bank Of India, IFSC Code: SBIN0004113



TDS PAYMENT INFORMATION

COMPANY AND TDS FILLING DETAILS

Company Name

Lohia Developers (India) Private Limited

Company PAN

AAACL5169Q

ADDRESS AND CONTACT DETAILS

Registered Address

Lakri Fazalpur, Delhi Road,
Moradabad, Uttar Pradesh

Postal Address

Lakri Fazalpur
Delhi Road, Moradabad, Uttar Pradesh

Email Id

lohiadevelopers@yahoo.com

Contact

+91 9990 966 609

INFORMATION AND TUTORIALS

TDS Filing Tutorial

<https://www.incometaxindia.gov.in/tutorials>

Income Tax Compliance Portal

<https://www.incometax.gov.in/iec/foportal/>

Generate Income Tax Form 141 (Earlier Form 26QB)

<https://www.incometax.gov.in/iec/foportal/help/all-topics/e-filing-services/form-141-challan-cum-statement-deduction-tax-us-3931-UM>

Generate Income Tax Form 132 (Earlier Form 16B)

<chrome-extension://efaidnbmnnnibpcajpcglclefindmkaj/https://www.incometaxindia.gov.in/documents/d/guest/fn-130-131-132-133>

For all official TDS payments, use the details provided for our records and for submitting the tax payment. Please contact the company directly if you have any questions or require further information regarding TDS payments.

FINANCE PARTNERS



YOUR CUSTOMER PORTAL

Everything You Need in One Place

Please find below the details that can be viewed and checked through the Customer Portal at:

 <https://server1.farvisioncloud.com/>



Note: For Username & Password please refer to the welcome letter.

Customer Info Section

Home
Applicant Ledger
Outstanding
Late Payment Fee Ledger
Statement of Account
My Generic Document
Project Progress

Document Print Section

Receipt Print
Invoice Print

Attachment Section

Document Attachment

My Queries Section

Query

For your convenience, all the above information is available in the portal link provided.

CONTACT US

CRM Email: crm@lohiaworldspace.com

Contact Person

Mr. Ambuj Tomar
+91 9990 966 609

Scan QR or click *



Customer Testimonials



Township Walkthrough



Founders message



Brand Film



EXCLUSIVE
VILLA COMMUNITY.

Experience Center (Site Office)

Lohia One, Opposite Sector 6,
New Moradabad,
Uttar Pradesh - 244102

Lohia Developers (India) Pvt. Ltd.

3rd Floor, Centrum Plaza Mall,
Khasra No 369-370, Opp. Metro Pillar 16B,
MG Road, Sultanpur, New Delhi, 110030

+91 70 80 90 60 60

Scan QR or click *



lohiaworldspace.com



Township Location

CLICK ICONS TO VISIT
OUR SOCIAL HANDELS

